Construction schedule - Education and Community Center, Pnea Pon

2016

Nr	Task	Day	Start	End
01	Footing & Piling	20	01.02.	20.02.
02	Subtic tank	10	21.02	03.03.
03	Baseplate	17	04.03.	20.03.
04	Piling GF	10	21.03.	30.03.
05	Brick GF / Rain Water tank	25	31.03.	24.04.
06	Steel Construction f. ceiling	20	25.04.	16.05.
07	Ceiling GF	30	17.05.	15.06.
08	Electric / Water GF	10	16.06.	25.06.
09	Plastering GF	10	26.06.	05.07.
10	Tiles GF	15	06.07.	20.07.
11	Bathrooms GF	10	21.07.	31.07.
12	Doors / Windows GF	7	01.08.	07.08.
13	Painting GF inside	7	08.08.	14.08.
14	Cleaning	1	15.08.	15.08.
15	Piling 1ST	25	16.08.	11.09.
16	Roof Counstruction + Tiles	20	12.09.	03.10.
17	Construction f. Water Tanks	7	04.10.	10.10.
18	Rainwater System	7	11.10.	17.10.
19	Cleaning	1	18.10.	18.10.
20	Brick 1ST	15	19.10.	04.11.
21	Electric / Water 1ST	10	05.11.	14.11.
22	Plastering 1ST	10	15.11.	24.11.
23	Tiles 1ST	15	25.11.	09.12.
24	Bathrooms 1ST	10	10.12.	19.12.
25	Doors / Windows GF	7	20.12.	27.12.
26	Painting 1ST inside	7	02.01.	08.01.
27	Painting All Outside	14	09.01.	22.01.
28	Cleaning IN & OUT	2	23.01.	24.01.

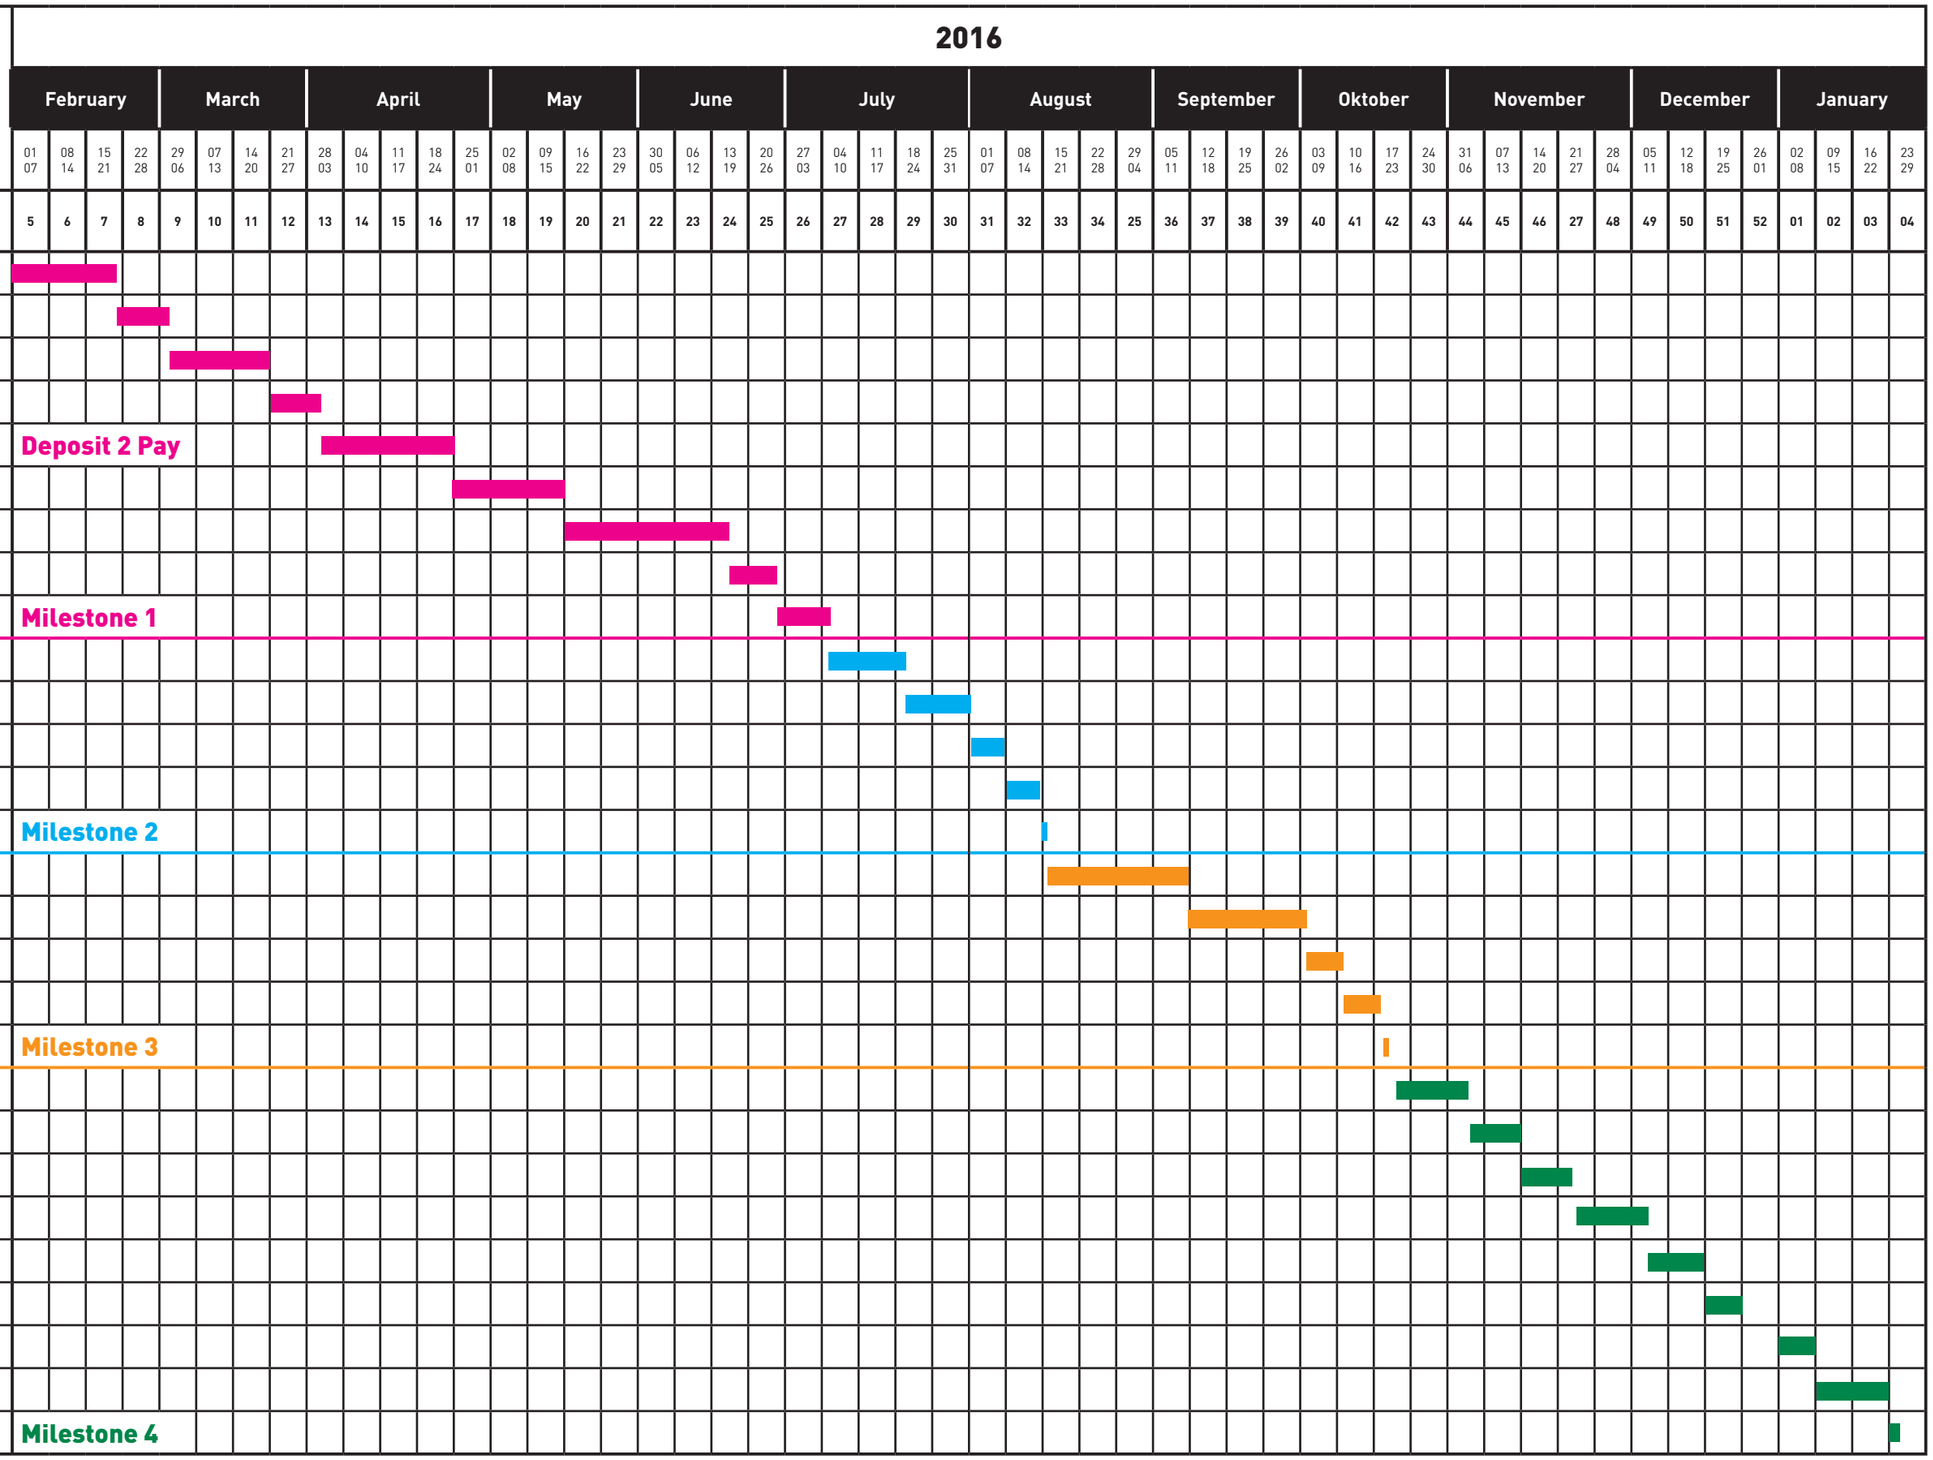

GF: Ground Floor 1ST: First Floor 2ND: Second Floor RF: Roof Floor

Save poor Children in Asia Organization, 2139 Phnom Boeng Chhouk, Sangkat Kilomet No.6, Khan Russey, Phnom Penh, Kingdom of Cambodia
